BRUHAT BENGALURU

Clients Name : Executive Engineer Byatarayanapua Division
Project Name : PACKAGE-1, INCLUDES 3 WORKS OF RS.200.00 LAKHS 1) IMI
IMPROVEMENTS TO ROADS AND DRAINS AT MANJUNATHI
9TH CROSS TO 13TH CROSS IN WARD NO.06 BYATARAYAN

Consultants : Rudraprasad Consultants
Project Manager /Team Leader : Karthik Rechan
Project Start Date : 23-Jul-18
Project End Date : 23-Nov-18
Project Length in Months : 4 months

Sl. No	Assignment	Unit	Boq Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Earthwork excavation by manual means in ordinary soil	Cum	2060.33	1752.09	85	25-07-18	23-11-18	121
2	Providing granite slabs of selected quality roughly dressed having a size of 7.5cms thick and fixed in cement mortar (1:6)	Sqm	1008.45	350.73	35	05-08-18	23-11-18	110
3	Excavation for roadwork in soil with hydraulic excavator of 0.90 cum bucket capacity	Cum	1616.11	1592.10	99	27-07-18	23-11-18	119
4	Providing and laying in position plain cement concrete of mix 1:3:6	Cum	369.62	285.90	77	04-08-18	23-11-18	111
5	Cement concrete pavement.Construction of un-reinforced plain cement concrete pavement, thickness as per design, over a prepared sub base with OPC cement or any other type as per clause 1051.2.2 design mix M20/M30	Cum	446.45	351.12	79	06-08-18	23-11-18	109
6	Vaccum de-watering with vaccum pump and suction mat and compaction with skin floater	Sqm	2976.30	2835.99	95	06-08-18	23-11-18	109
7	Providing,laying, spreading and compacting wet mix macadam	Cum	1662.93	1283.30	77	29-07-18	23-11-18	117
8	Cleaning the existing black topped surface.	Sqm	23771.00	20722.03	87	03-08-18	23-11-18	112
9	Providing and applying tack coat using 80/100 grade bitumen (VG10) on prepared black topped surfaces	Sqm	27873.50	21941.28	79	06-08-18	23-11-18	109
10	Providing and laying bituminous concrete 40 mm	Cum	1114.94	879.69	79	06-08-18	23-11-18	109
11	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface	Sqm	882.20	739.90	84	03-09-18	23-11-18	81
12	Construction of embankment with material gravel/murrum.	Cum	423.50	0.00	0	01-08-18	23-11-18	114

MAHANAGARA PALIKE

?ROVEMENTS TO ROADS AND DRAINS AT SADIQ LAYOUT(DEFENCE LAYOUT) IN WARD NO.06 BYATARAYANAPURA SUB DIVISION. 2) NAGARA IN WARD NO.06 BYATARAYANAPURA SUB DIVISION. 3) IMPROVEMENTS OF DRAINS AND RCC CULVERTS AT HEGADENAGARA APURA SUB DIVISION.

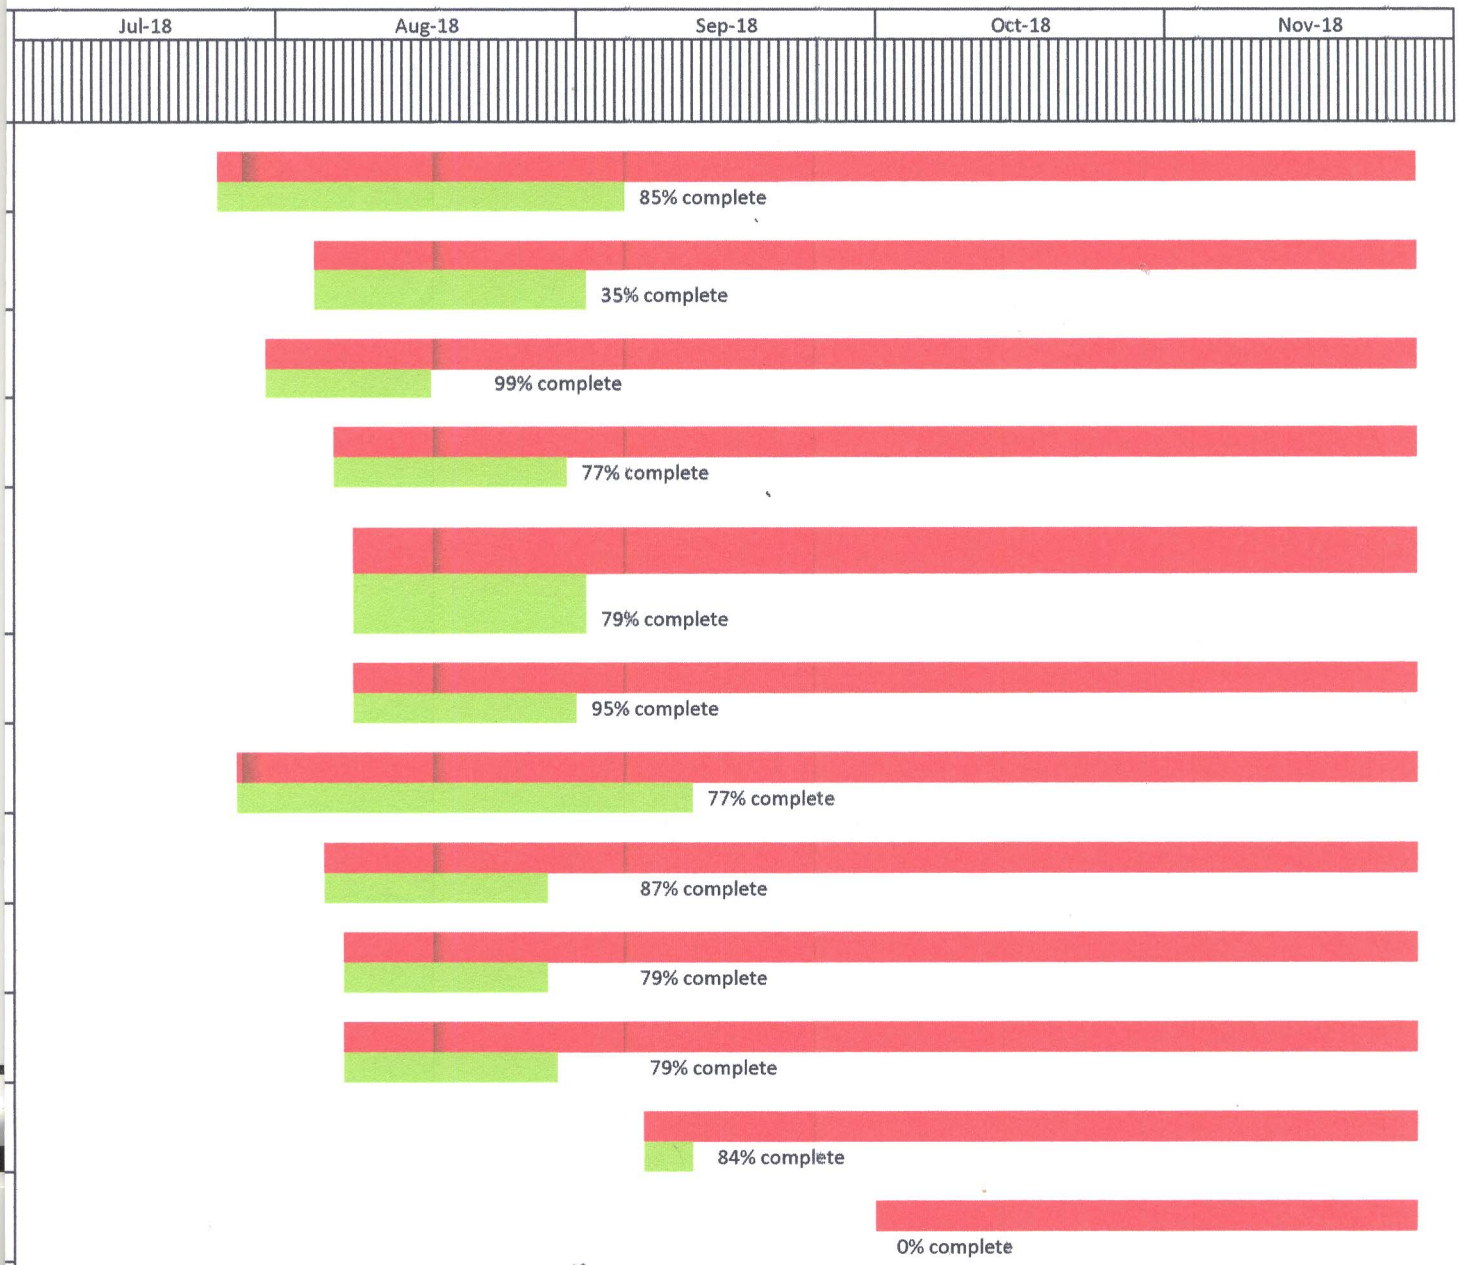

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-26
